



Bull Run
TREATMENT
PROJECTS

*Our water: Safe and abundant
for generations to come*

PORTLAND WATER BUREAU

Bull Run Filtration Project

Informational Meeting

April 9, 2026



Agenda

1. Welcome & Project Overview
2. Pipeline Construction Updates
3. Facility Construction Updates
4. Questions & Comments




Bull Run Filtration project update

- February 2026 LUBA decision affirmed Multnomah County's approval of the project land use permits
- Adjusted project schedule and budget and shared updates with City Council, Portland Utility Board, and the community
- Continuing coordination with City of Sandy on new water infrastructure, including new pipeline along Bluff Road and proposed pump station at facility site




Schedule update

- In March, Oregon Health Authority let us know they plan to revise the Bilateral Compliance Agreement with the extended deadline of September 30, 2029
- Typical construction hours are Monday through Saturday 7 am to 6 pm to help maintain schedule

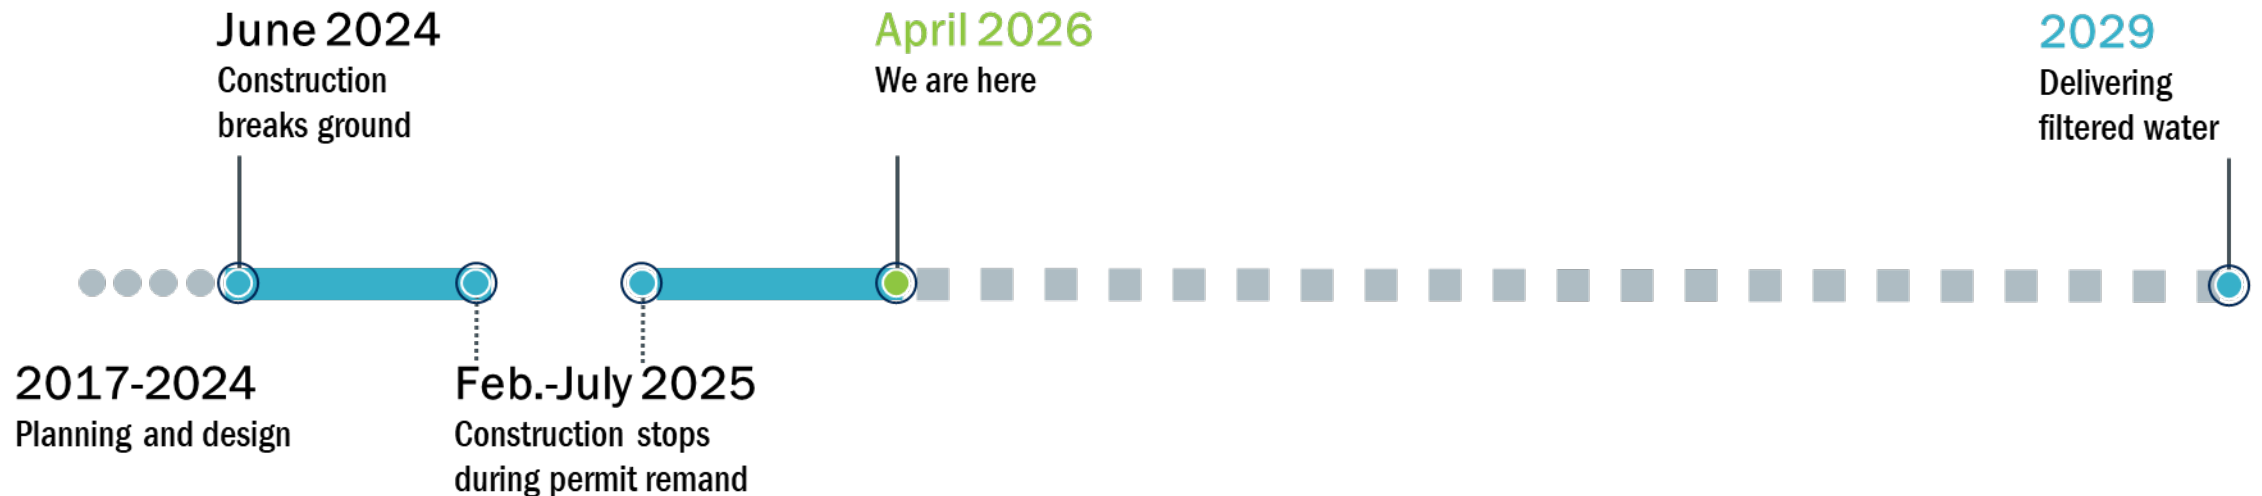

Project pipelines overview

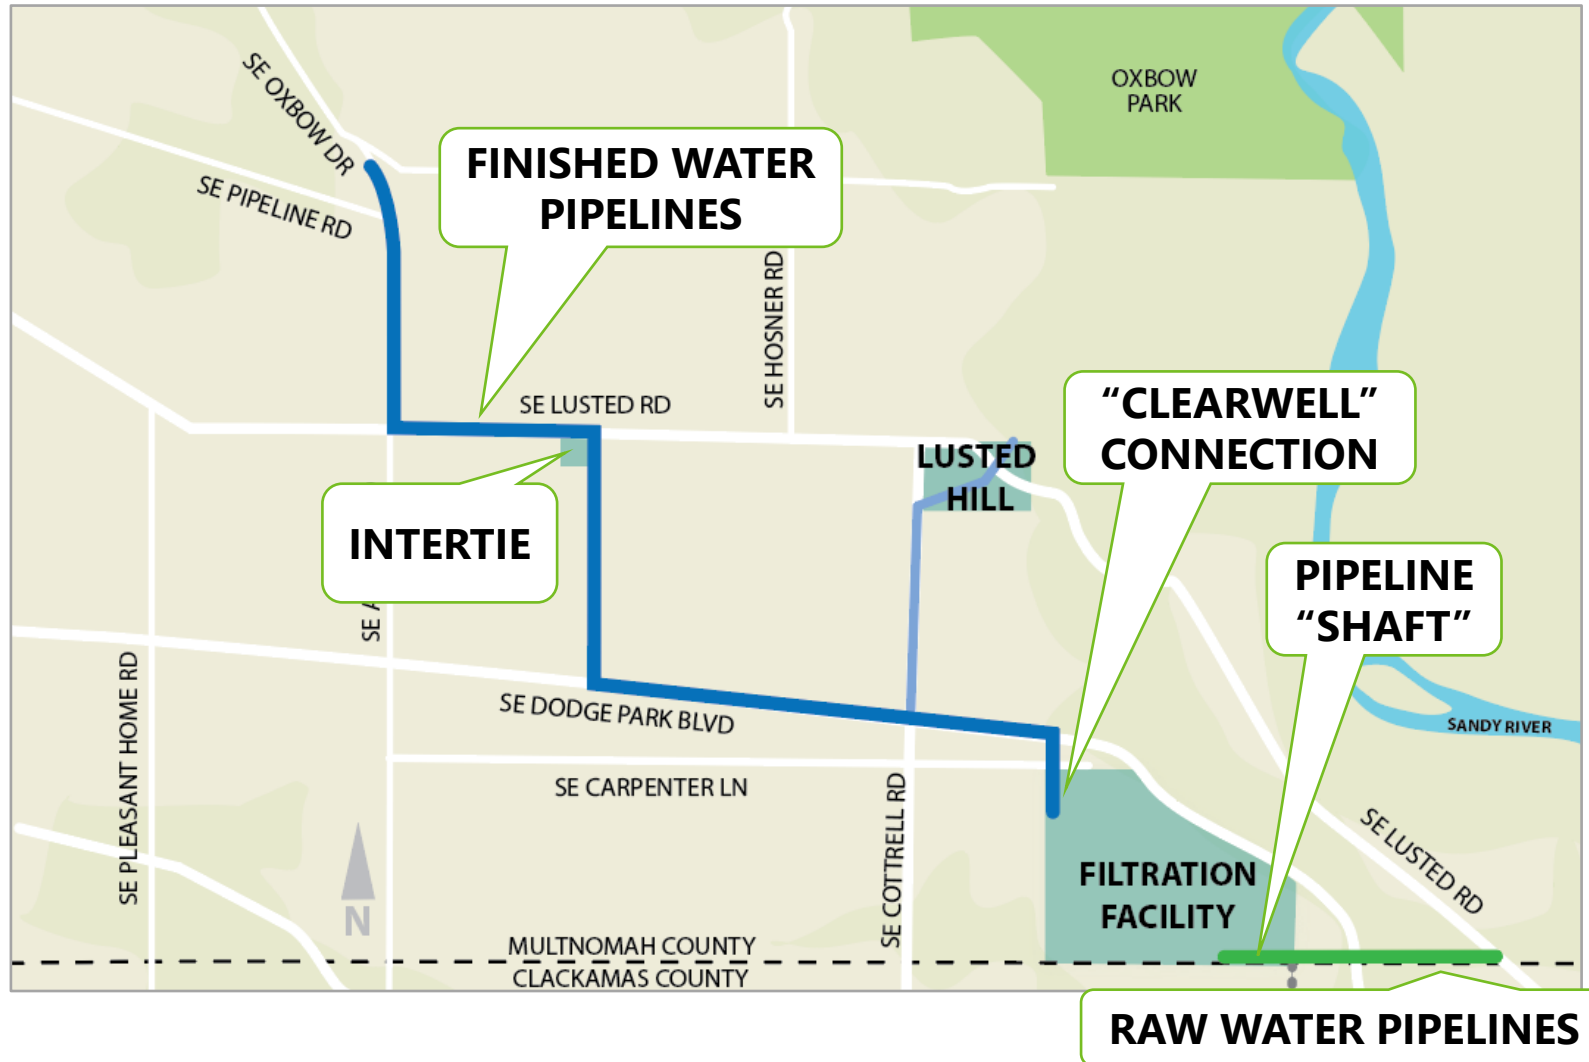

Raw Water Pipelines:

- Two new pipes will tie in at "lower" Lusted with existing water conduits, then tunnel uphill to facility site

Finished Water Pipelines:

- One new pipe from facility follows Dodge Park, then crosses easement to intertie
- New pipes from intertie will follow "upper" Lusted, then Altman to tie in near Pipeline and Oxbow with existing water conduits

Water filtration facility looking east



Pipeline construction overview



30%
complete

- ✓ Completed Pleasant Home Water District main installation
- ✓ Installed **9,500+** linear feet of pipe to date
- ✓ Completed finished water pipe tunnel
- ✓ Completed slab-on-grade work at intertie
- ✓ Excavated **325** feet of raw water tunnel to date


FINISHED WATER PIPELINES

Pipeline clearwell connection completed

- Excavated under Carpenter Lane to connect new pipeline to the “clearwell” (underground storage for filtered water)



Pipeline tunneling construction (Feb. 2026).

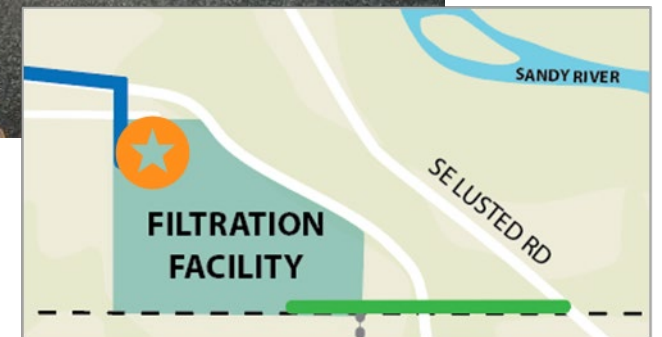

FINISHED WATER PIPELINES

Finished water intertie progress

- Finished slab-on-grade work, starting vertical rebar work
- Intertie facility will include:
 - Landscaped site with a small building above ground (modeled view shown right)
 - An underground vault with valves and pipeline interconnections



Finished water intertie construction (April 2026).



Finished water intertie concept rendering.

RAW WATER PIPELINES

Pipeline tunneling work ongoing


- Excavating two tunnels where new pipelines will be installed
- Tunnel one excavation is at 325+ ft so far
- Tunnel two excavation will start in late April
 - Increased activity with more work crews accessing site
 - Additional equipment noise until machine gets deeper into tunnel



RAW WATER PIPELINES

Pipeline shaft excavation progress

- Excavating 237 ft shaft in southeast corner of facility site (166+ ft so far)
- Planning some controlled blasts during excavation
- Blasting may start early in May, will happen during shift hours and be spaced over several weeks
- Safety will be a priority throughout
- Noise and vibration from each blast will last a few seconds and will be monitored
- Neighbors can sign up for pre-blast notices


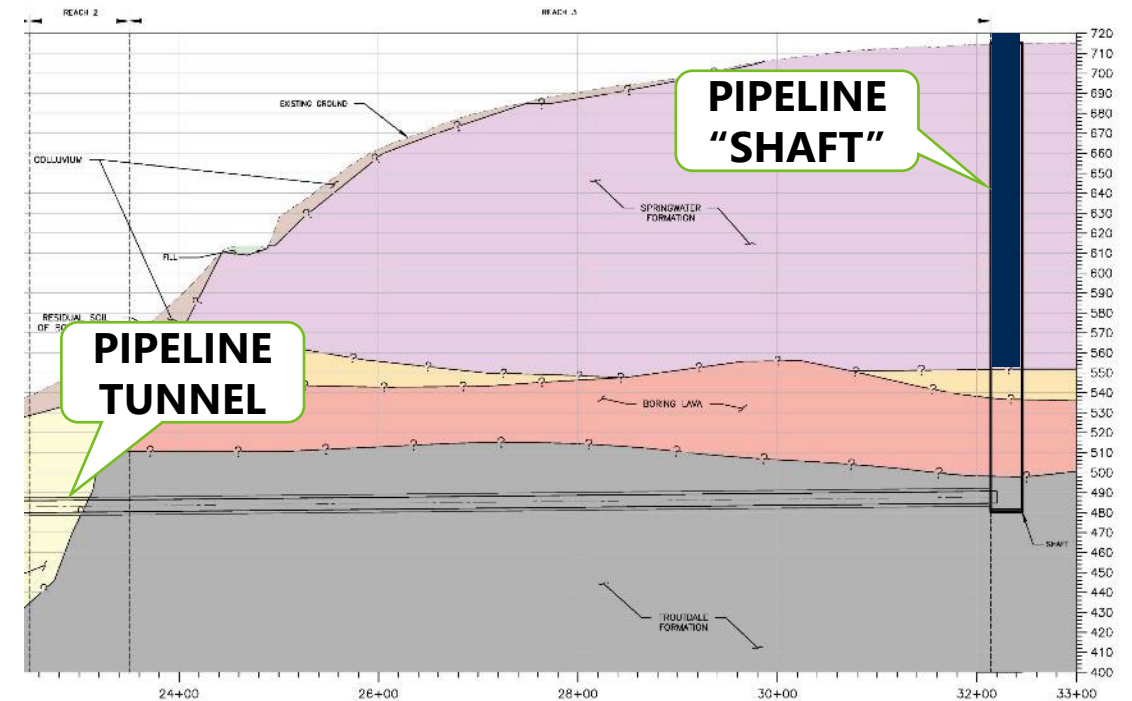


Note: The bottom of the tunnel shaft is designed to be more than 75ft above the elevation of the shallowest well.

RAW WATER PIPELINES

Lusted Road pipeline connection

- Ongoing pipeline connection construction through late June
- Mobilizing piling equipment late April, onsite 2-3 weeks
- Full closure on Lusted Road during work hours for safety
 - Temporary traffic lights outside of work hours
 - Buses and emergency vehicles have access through the closure

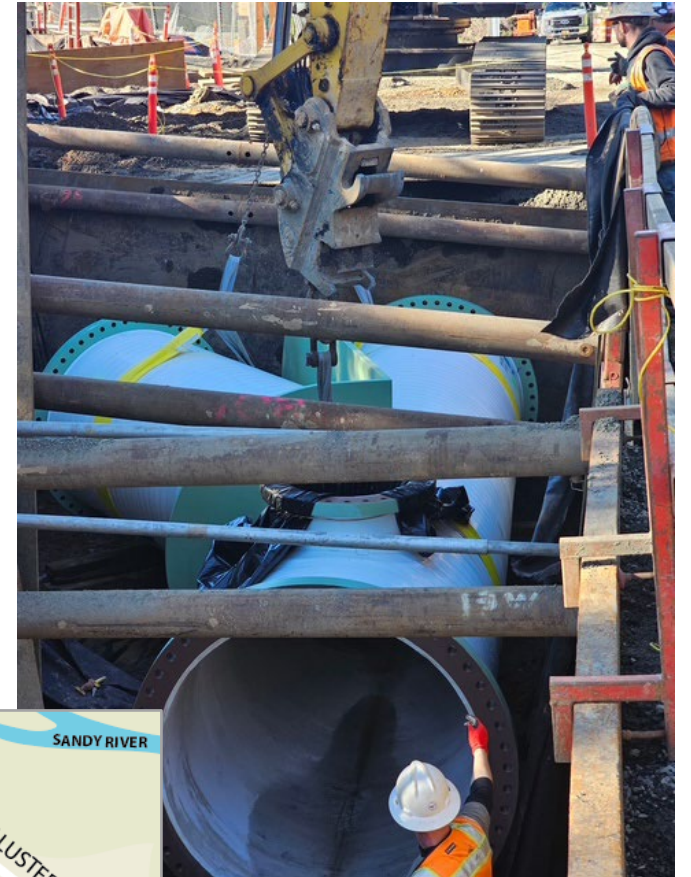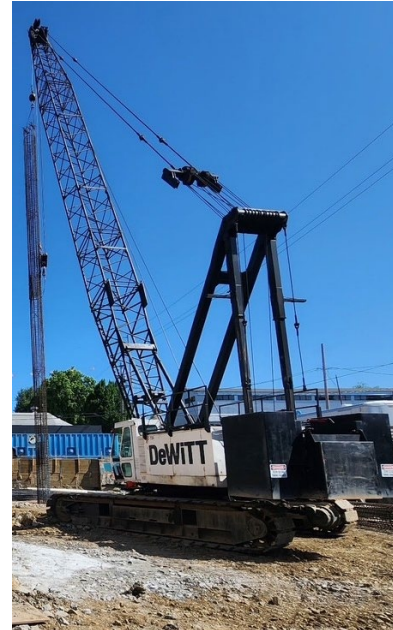

Pipeline construction on Lusted Road (March 2026).

FINISHED WATER PIPELINES

Lusted Road improvements

- Pipeline construction ongoing
- In May/June, planning road improvements to widen north side, patch existing road
- Then Lusted Road will reopen to normal traffic flow



Pipeline construction on Lusted Road (March 2026).

Upcoming pipeline work

May/June 2026:

- Wrap up current pipeline installation work on upper Lusted Road and lower Lusted Road

July 2026:

- Start installing new pipeline at Oxbow Drive/Altman Road intersection
- Restart pipeline work along Dodge Park Boulevard west of Cottrell Road

Fall 2026:

- Restart pipeline work along Dodge Park Boulevard east of Cottrell Road



Facility construction progress



25%
complete

- ✓ Completed mass excavation and grading
- ✓ Installed **3,200** linear feet of pipeline to date, including 72-inch diameter pipe
- ✓ Poured **5,600** cubic yards of structural concrete to date
- ✓ Shifted to bussing/vanpooling for craftworkers (232 craft onsite currently)

Facility construction progress



Looking south across facility construction site (March 2026).



Filtration and sedimentation treatment basin construction (March 2026).

Upcoming facility work

- Continuing concrete pours for treatment basins and buried pipe encasements
- Continuing to pour slabs for buildings that will support facility operations and maintenance
- Transitioning from generators to utility construction power
- Starting installation of 108-inch diameter onsite raw water pipe




Bull Run
TREATMENT
PROJECTS

Questions and Comments

Get regular e-news notices on construction

- Visit **portland.gov/brtpnews** to update your preferences
- Scroll down to find Bull Run Filtration project e-news options
- Add **water@info.portland.gov** to your email contact list





Portland Water Bureau newsletters

All subscribers receive a monthly newsletter with general information about their drinking water.

Sign up for updates about other projects and programs by checking the boxes next to the item(s) that interest you below.

Email *

name@example.com

What is your first name?

Bull Run Filtration project updates


- Monthly project updates
- Neighbor updates (traffic, sound, or related construction work information)
- Meeting notifications

Scroll down



Get construction traffic-related text alerts

- Sign up to get text notices about lane closures or other construction traffic information
- Visit:
portland.gov/water/filtrationtxts
- Texts will come from 833.858.2354



Portland Water Bureau
FROM FOREST TO FAUCET

Bull Run Filtration Construction Text Alerts

Sign up to receive text notifications about temporary lane closures and other construction traffic information related to the Bull Run Filtration project.

Phone *

+1

What is your first name?

For project information...

Call: 503.823.1505

Email: bullrunprojects@portlandoregon.gov

Visit: portland.gov/FiltrationConstruction

Attend: May 14 Coffee with the Contractor (in-person)

June 11 Coffee with the Contractor (in-person)

July 16 Neighbor Update Meeting (online)





Bull Run
TREATMENT
PROJECTS

*Our water: Safe and abundant
for generations to come*

Thank you!

Learn More portland.gov/bullrunprojects
